

Jefferson High School **EXECUTIVE SUMMARY**

PROVIDED BY FINDORFF

Overview

School is well under way at the Jefferson High School, while construction winds into the final month of scheduled work. Final MEPF (Mechanical, Electrical, Plumbing, & Fire Protection) fixtures are being installed at the Skills Lab Addition as painting chases those runs with specified colors for each individual system. This will highlight how these systems coexist and the sequence for each within a building. Final architectural and MEPF finishes are being put in place in the Head House/Test Kitchen and all Shop areas, as well. As new equipment rolls in for the Shop spaces and the Skills Lab Addition, these items are being powered up and ducted for use in the coming month. The end product is near, we are excited to bring this project to a close shortly!

Progress Update

- MEPF fixtures/devices in the Shop spaces, Head House/Test Kitchen, and Skills Lab Addition
- MEPF fixtures/devices painted in Skills Lab Addition
- Painting at the Shop spaces and Skills Lab Addition
- Mezzanine installation at the Skills Lab Addition
- Equipment move-in into Auto/Metal/Wood Shops

Upcoming Work

- Sealed concrete flooring in the Skills Lab Addition
- Mechanical unit startup in the Shop areas and Skills Lab Addition
- Final cleaning in all areas of construction

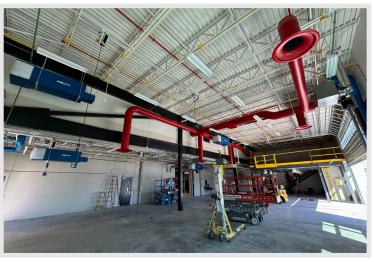


Photo of the various colors being painted on to identify the different MEPF systems being installed at the Skills Lab Addition.



Equipment is being set and hooked up for use in the Wood Shop and neighboring shops. Almost ready to get school projects started!

DID YOU KNOW?

The newest piece of equipment has recently been installed in the Skills Lab staging construction materials or even teaching classes.



Questions?

Project Manager, Jonathan Winch / (608) 219-5091 / jwinch@findorff.com Project Engineer, Brennan Sullivan / (920) 319-2077 / bsullivan@findorff.com

